

Area Planning Branch - No.1 (N.Staffs).

See Distribution.

Chatterley Whitfield Colliery
8690' Horizon Middle Pit Connection.

16th October, 1963.

Please find enclosed one copy of the phasing and progress chart,
as agreed at the No.1 Group Meeting held on the 9th October.


A. Leaming

(A. Leaming).

No.1 Group Planning Engineer.

Copies to:- Messrs. W.T.Archer, P.Smallman, G.A.Haslett,
D.Harrison, R.Walley.

CW/15/30

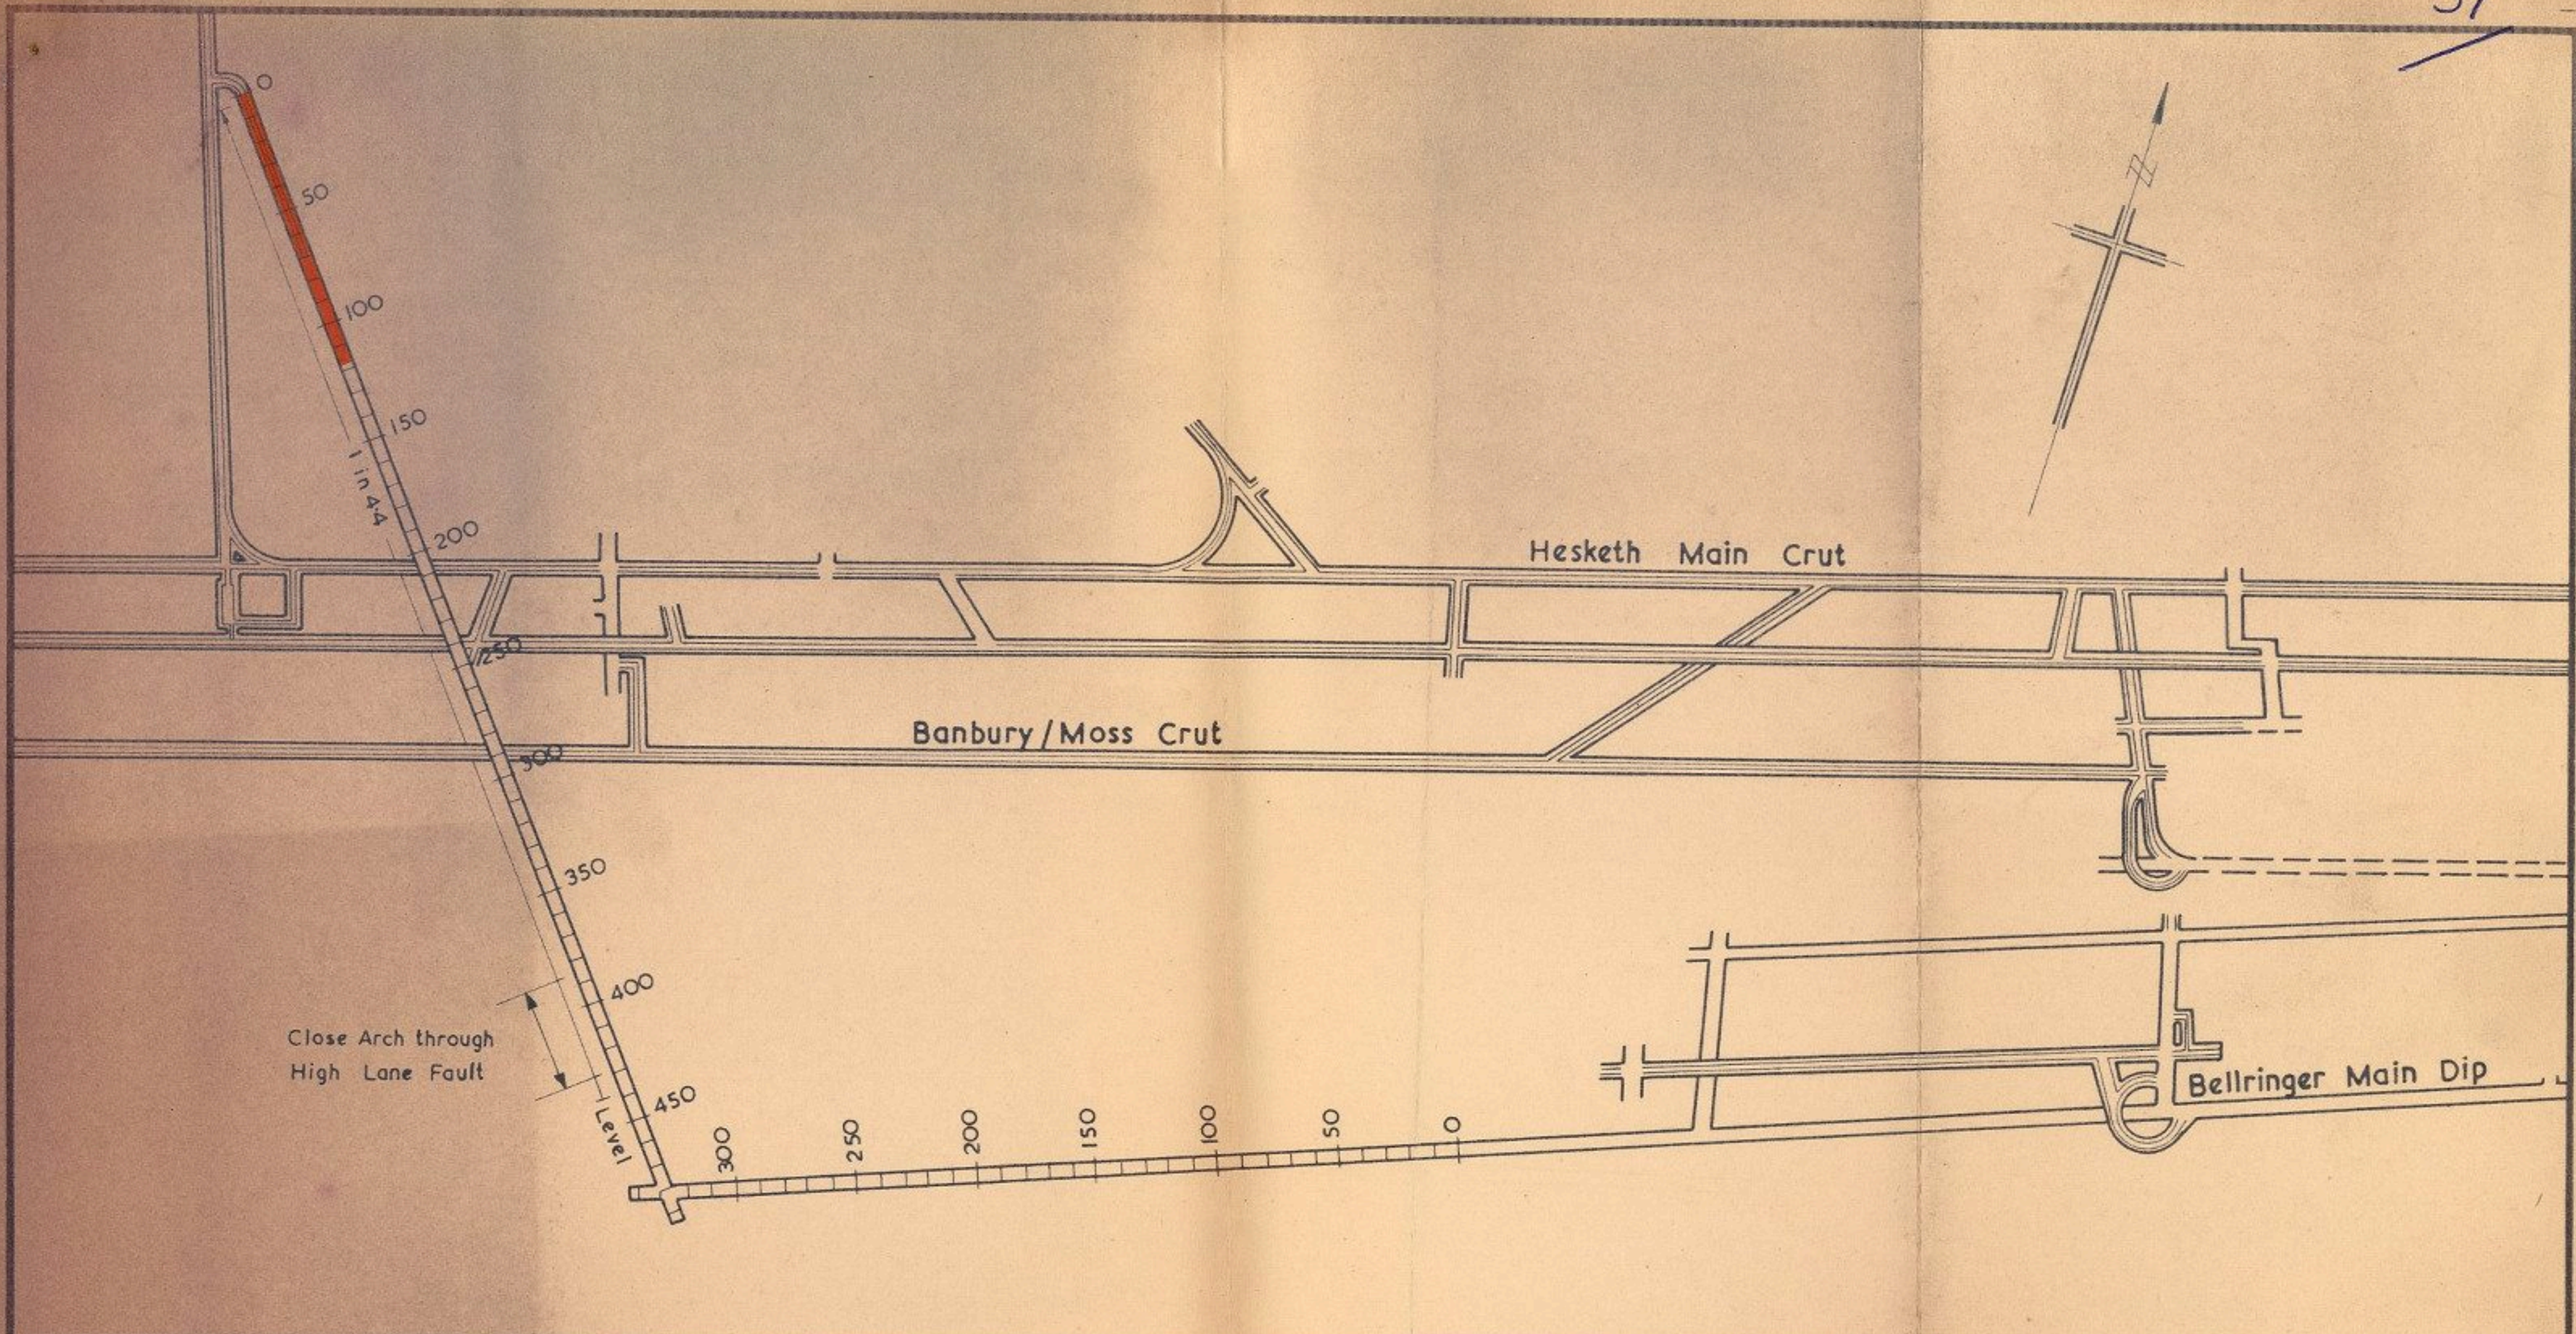


Description	1963												1964																											
	OCTOBER				NOVEMBER				DECEMBER				JANUARY				FEBRUARY				MARCH				APRIL				MAY											
	28	5	12	19	26	2	9	16	23	30	7	14	21	28	4	11	18	25	1	8	15	22	29	7	14	21	28	4	11	18	25	2	9	16	23					
1 IN 4-4 RISE CRUT - 1/740/17/31 - AT 20 YDS/WK	90	110	130	150	170	190	210	230	250	270	290	310	330	340	360	380	395	410	425	440	460	480	496																	
JUNCTION - BOTTOM OF BELLRINGER MAIN DIP																																								
BELLRINGER MAIN DIP EXTENSION - AT 15 YDS/WK																																								

PHASING AGREED AT No. 1 GROUP MEETING - 9th OCTOBER 1963
 BY MESSRS. W. WILCOX, R. W. SCURFIELD, G. E. HEWITT, W. T. ARCHER, P. SMALLMAN.

NATIONAL COAL BOARD
 WEST MIDLANDS DIVISION No. 1 NORTH STAFFS AREA

CHATTERLEY WHITFIELD COLLIERY
 8690'-HORIZON MIDDLE PIT CONNECTION
 PHASING & PROGRESS CHART

DRAWN BY	A.A.L.	SCALE	AREA PLANNING OFF
TRACED BY	K.A.	1/2500	DRAWING No.
CHECKED BY		DATE	2148/50
PASSED BY			



Junction Bottom Staple Shaft
 Staple Shaft 30 Yds.
 Junction Top Staple Shaft
 Staple Shaft Borehole 30 Yds.

Junction Construction
 Phased to Commence
 14th. Sept. 1959

CONNECTION JOB No. 05-18 (Including 19,20 & 21) PHASED AT AVERAGE OF 15 YDS/WEEK
 —Do— 18-07 —Do— 20 —Do—
 JOB No. SHEWN 01

NATIONAL COAL BOARD			
WEST MIDLANDS DIVISION		No. 1 NORTH STAFFS AREA	
CHATTERLEY WHITFIELD COLLIERY			
8300 Ft. Horizon - Phasing & Progress			
DRAWN BY	A.A.L.	SCALE	AREA PLANNING OFF
TRACED BY	A.A.L.	1-2500	DRAWING No.
CHECKED BY	A.A.L.	DATE	1366/50
PASSED BY		SEPTEMBER 1959	
